




*Cable terminations inside WTG in progress*



*Wind farm substation cabling trenches*

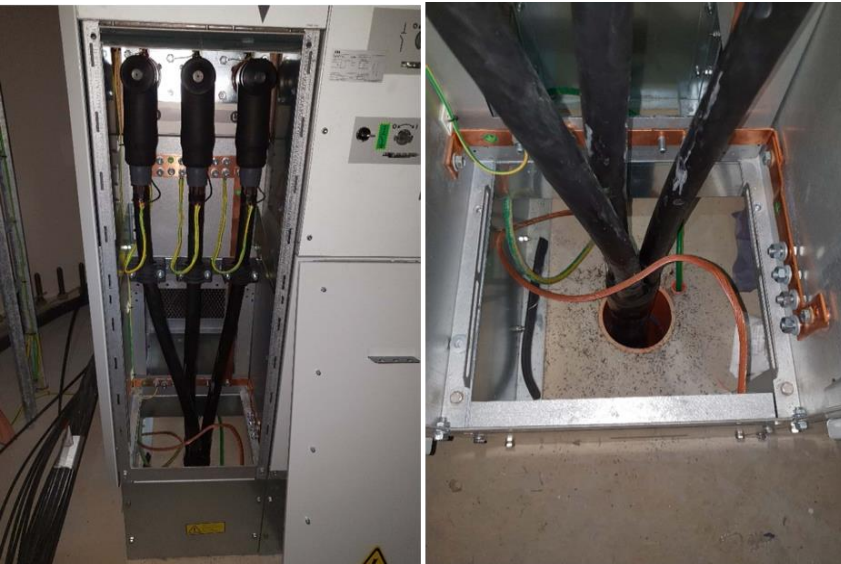

*WTG32 - Excavation and access road*



*Wind farm substation powerline landing structures*

- 21 of 53 WTG now complete. 28 WTG base and mid tower sections erected.
- 53% of the turbine components (blades, hubs, towers) delivered to site. Internal road repairs completed to allow deliveries to tower sites. Port-Site deliveries remain on-hold due to wet weather.
- 50 of 53 foundations poured. Excavation and preparation of foundations continuing. Backfilling and earthing of poured foundations continues.
- Continuation of earthworks for turbine access roads; approximately 89% of clearance works complete
- Construction of substation and switchyard continuing.
- Placement of underground cabling continuing
- Works continue on upgrades to Site Entry Road (intersection to site compound) including vegetation of batters
- UXO, Cultural Heritage and Environmental aspects continue prior to vegetation clearance in new areas.
- Weed contractor has commenced to address issues following recent rainfall.
- Personnel on-site averaged 238.
